


JJ White Construction Logistics

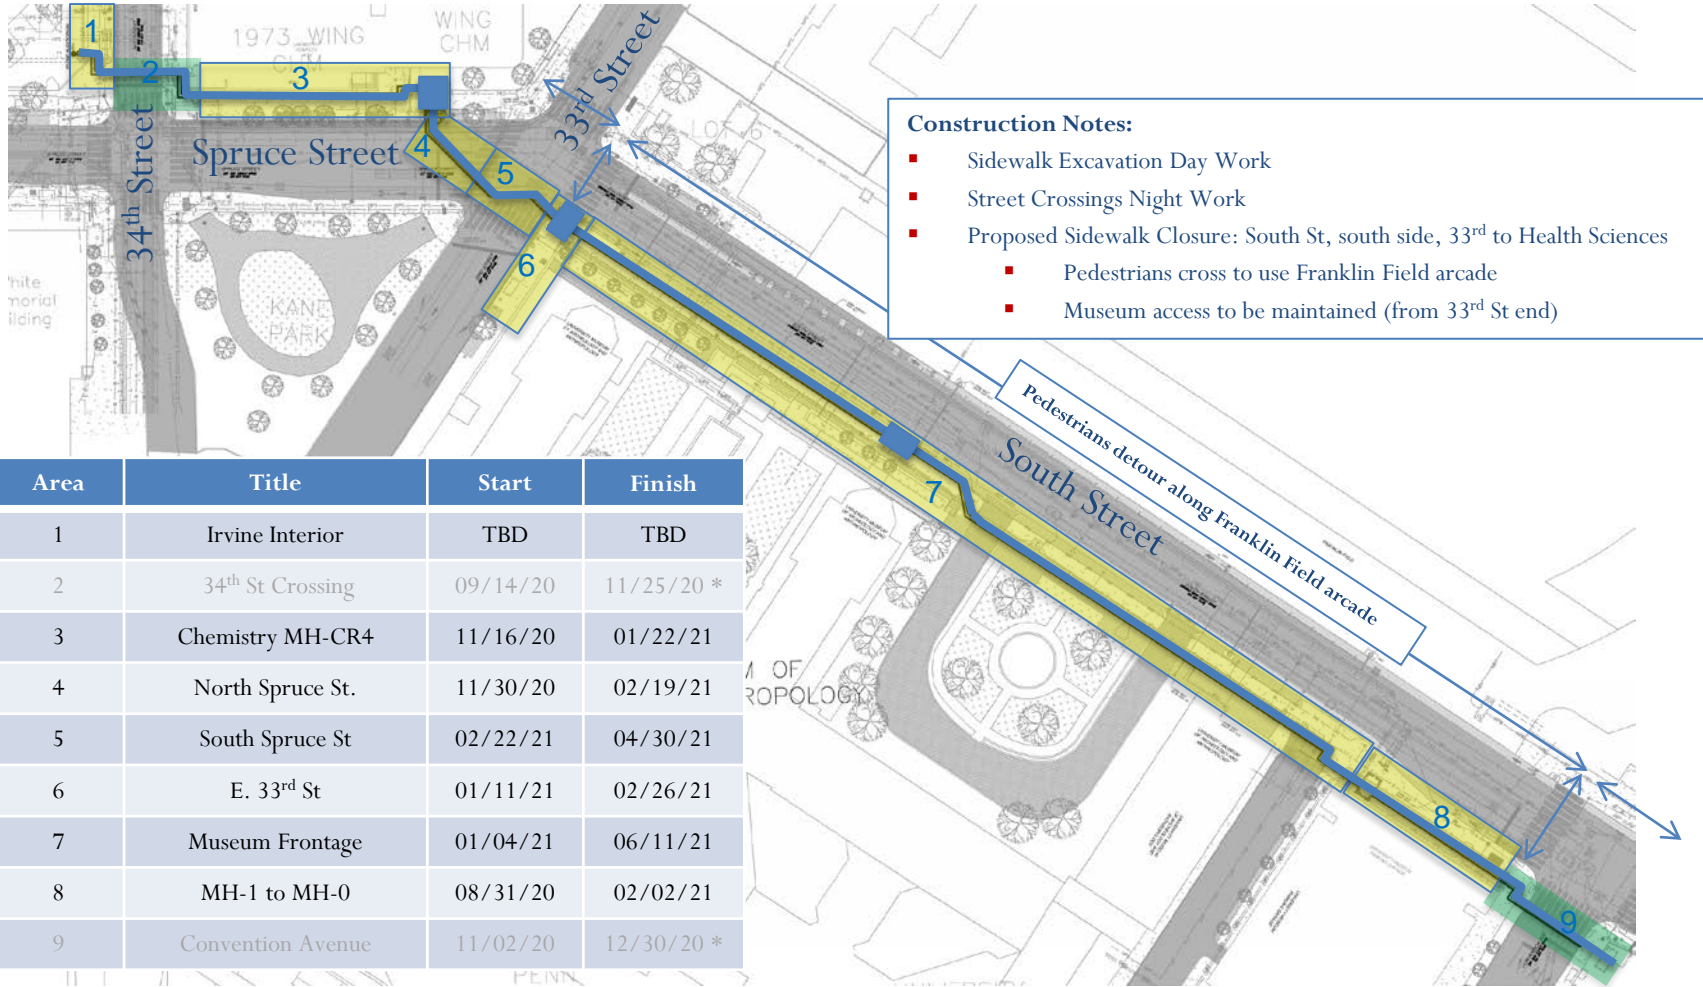

Area	Title	Start	Finish
1	Irvine Interior	TBD	TBD
2	34 th St Crossing	09/14/20	11/25/20 *
3	Chemistry MH-CR4	11/16/20	01/22/21
4	North Spruce St.	11/30/20	02/19/21
5	South Spruce St	02/22/21	04/30/21
6	E. 33 rd St	01/11/21	02/26/21
7	Museum Frontage	01/04/21	06/11/21
8	MH-1 to MH-0	08/31/20	02/02/21
9	Convention Avenue	11/02/20	12/30/20 *

*Area Complete
